

CCS Documentation Status Report

Sprint 26.19 · 10–23 September 2026 · Report date 23 September 2026 (all content illustrative)

To	CCS SW Lead; Program CM	From	Nathan B. Smith, Technical Writer
Release	CCS 4.2.1 (illustrative)	Jira board	CCSDOC, 2-week sprints
Overall status	YELLOW on schedule, one risk		
		Next report	7 October 2026 (end of Sprint 26.20)

No CUI, classified, proprietary, or export-controlled information is contained in this document. Provided as a technical writing sample — Nathan B. Smith.

Bottom line: 29 of 34 committed points done (85%). SUM Revision B and the 4.2.1 VDD are on track for the 20 October release. The How-To Guide walkthroughs are behind by 5 points because test-build time was lost to a lab outage; recovery plan below.

- **Decision needed:** approve 2 extra hours of test-build time on 30 Sep for How-To walkthroughs (Risk R-1).
- **Requirements database:** 42 requirements updated, 11 issues closed, traceability at 96% (target 95%).

29 / 34

Story points done / committed

14

Jira tickets closed


96%

Requirements traced to tests (target 95%)


2

Release media packages built and logged

Sprint burndown (story points remaining)

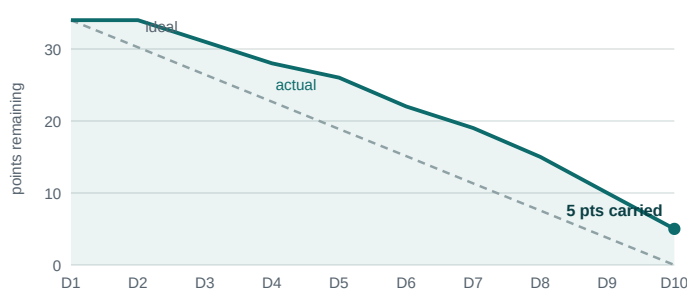

Velocity, last five sprints (points completed)

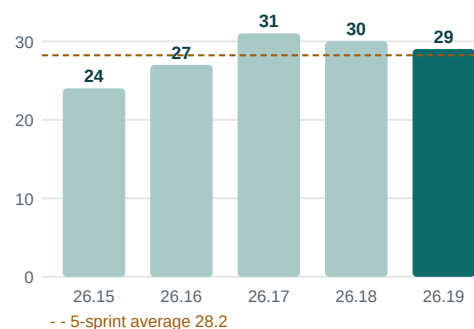

Deliverable status

Deliverable	This sprint	Progress	Due	Status
SUM, Revision B	Sections 5.3.1–5.3.3 updated for 4.2.1 changes; SME review done	Sections 1–5 of 6	20 Oct	ON TRACK
How-To Guides	3 new guides drafted; walkthroughs for 2 not run (lab outage)	18 of 25 published	20 Oct	AT RISK
Version Description Document 4.2.1	Drafted from build manifest and Jira fix version	Draft complete	13 Oct	ON TRACK
Site Installation Guide, Rev B	Rollback section updated; no other changes needed	Complete	20 Oct	DONE
Training Lesson 2.1	Job sheet steps aligned to new route editor labels	Complete	—	DONE

Jira tickets closed this sprint

Key	Summary	Type	Points
CCSD0C-412	SUM 5.3.1.2: update route editor steps for new Validate button	Story	5
CCSD0C-415	SUM 5.7: add messages CCS-C-310 through CCS-C-314	Story	3
CCSD0C-417	How-To: Transfer control (draft, SME review)	Story	3
CCSD0C-418	How-To: Task a sensor (draft, SME review)	Story	3
CCSD0C-419	How-To: Lost link (draft, walkthrough, review)	Story	5
CCSD0C-421	VDD 4.2.1: first draft from build 4.2.1-1204 manifest	Story	5
CCSD0C-423	ICG section 8: rollback command changed	Story	2
CCSD0C-424	Build and log release media, 4.2.1 RC1 and RC2	Task	3
—	6 requirements-database update tasks (see below)	Task	—

Carried over to Sprint 26.20

Key	Summary	Points	Reason
CCSD0C-426	How-To: Transfer control, walkthrough on test build (follows CCSDOC-417)	3	Lab outage 17–18 Sep
CCSD0C-427	How-To: Task a sensor, walkthrough on test build (follows CCSDOC-418)	2	Lab outage 17–18 Sep

Requirements database updates

Changes recorded in Jira and reported from the Confluence requirements dashboard. Counts are for this sprint.

Item	Opened / added	Updated	Closed	Notes
Requirements	3	42	0	Updates reflect 4.2.1 change requests; 3 new from SCR-88
Issues (trouble reports)	7	15	11	Net open issues down from 26 to 22
Traceability links	18	—	—	Requirements traced to a test: 96% (target 95%)

Risks and issues

ID	Risk or issue	Impact	Mitigation	Owner	Status
R-1	How-To walkthroughs behind after lab outage	5 guides may slip past 20 Oct	Request 2 h extra test-build time 30 Sep; prioritize contingency guides	N. Smith	OPEN
R-2	UI labels may change again in 4.2.1 RC3	Rework of screenshots and steps	Freeze labels at RC3; screenshots taken last	SW Lead	WATCH
I-4	Two SME reviewers on leave 6–10 Oct	Review turnaround slows	Reviews scheduled before 3 Oct; backup SME named	N. Smith	MITIGATED

Plan for Sprint 26.20 (24 Sep - 7 Oct)

Planned work	Points
Carry-over walkthroughs (CCSDOC-426, -427)	5
How-To Guides: 4 remaining contingency guides	12
SUM Section 5.6 and 5.8 updates	5
VDD 4.2.1: final after RC3 build	3
Release media package, RC3	3
Requirements database: weekly updates	—

Commitment: 28 points, in line with the five-sprint average of 28.2.

Dependencies: RC3 build by 2 Oct; test-build time on 30 Sep (R-1).

Ceremonies: sprint review and retro 7 Oct; this report follows within 1 working day.

How these numbers are produced. Points and tickets: CCSDOC Jira board, filter `project = CCSDOC AND sprint = 26.19`. Requirements and issues: Confluence requirements dashboard. Traceability = requirements with a linked test ÷ active requirements. All names, keys, dates, and figures are illustrative.
